



**DC Repair Report**  
**FUTURE FUEL CHEMICAL**  
2800 GAP RD HWY 394 SO  
BATESVILLE, AR 72501

FolderID: 102566  
FormID: 19555044

**DC Repair Report Rev. 2**

**Location:** MOTOR SHOP LR  
**Job Number:** 102566  
**Serial Number:** WP-8-139-WP  
**Status:** Quarantine for review  
**Description:** 25HP 1150 RPM GE

**Hi-Speed Job Number:** 102566  
**Manufacturer:** GE  
**Product Number :** 5CD184ZA877B800  
**Serial Number:** WP-8-139-WP  
**HP/KW:** 75 (HP)  
**RPM:** 1150  
**Armature Voltage:** 92 (Volts)  
**Field Voltage:** 160 (Volts)  
**J-Box Included:** Yes

Priorities Found: ● **2 - High** ● **7 - Good**

**Overall Condition**




1. Describe the Overall Condition of the Equipment as Received  
*Serviceable*

P1





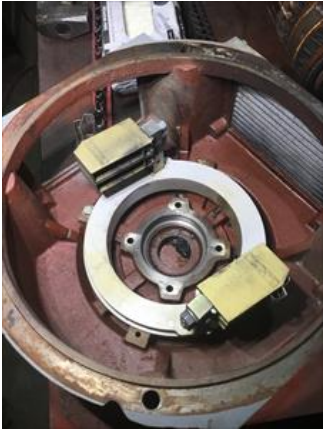

## 2. Nameplate Picture

P17





3. Distance From the End of the Shaft to the end of the Face of the Sheave/Coupling

**Initial Mechanical/Electrical**



- |                                      |         |     |
|--------------------------------------|---------|-----|
| ● 4. Does the Shaft Turn Freely?     | (Y) Yes |     |
| ● 5. Does Shaft Have Visible Damage? | (No) No | P22 |



6. Assembled Shaft Runout
7. Assembled Shaft End Play
8. Air Gap Variation <10%

- |                     |          |     |
|---------------------|----------|-----|
| ● 9. Lead Condition | (P) Pass | P55 |
|---------------------|----------|-----|



- |                       |          |
|-----------------------|----------|
| 10. Lead Length       | 6 Inches |
| ● 11. Frame Condition | (P) Pass |

Hi-Speed Industrial Service disclaims all warranties, both express and implied, relating to the information, reports, opinions and analysis disclosed to the Customer by Hi-Speed. Hi-Speed shall not be liable for any errors or omissions, or any losses, injury or damages arising from the use of such information, reports, opinions and analysis by the Customer.





13. Brush Information			P87
Brush Number	Quantity	Condition	
36A167402AA	4	replace	



14. Brush Holder Condition - Verify proper gap to Commutator	pass	P92
--	------	-----



Incoming Electrical Test





19. Total Field Ohms

48

P60



20. Field Ohms

P70

Between F1/F2

Between F3/F4

24.2

24.2



21. MegOhms between Fields and Series

22. Series Drop Test 1&2



Series 1

Series 2

23. Series Drop Test 3&4

Series 3

Series 4

24.	Field Drop Test Fields 1&2		
	Total AC Voltage	Field #1	Field #2
	<b>300</b>	<b>1.7</b>	<b>1.8</b>
25.	Field Drop Test Fields 3&4		
	Field #3	Field #4	
26.	Field Drop Test Fields 5&6		
	Field #5	Field #6	
27.	Field Drop Test Fields 7&8		
	Field #7	Field #8	
28.	Interpole Drop Test 1&2		
	Total AC Voltage	Interpole #1	Interpole #2
	<b>57</b>	<b>34</b>	<b>35</b>
29.	Interpole Drop Test 3&4		
	Interpole #3	Interpole #4	
30.	Interpole Drop Test 5&6		
	Interpole #5	Interpole #6	
31.	Interpole Drop Test 7&8		
	Interpole #7	Interpole #8	
32.	Armature Number of Bars - Bar to Bar Test		
	Number of Bars	Bar to Bar Test	
		<b>pass</b>	
<b>Mechanical Inspection</b>			
33.	Shaft Runout Drive End		<b>0.002 inches</b>
34.	Shaft Runout Armature		
	Drive End Bearing Journal	Armature Core	ODE Bearing Journal
35.	Drive End Bearing Number		<b>6211</b>
36.	Drive End Bearing Quantity		<b>1</b>
37.	Drive End Bearing Type		<b>(Ball) Ball Bearing</b>
			

Hi-Speed Industrial Service disclaims all warranties, both express and implied, relating to the information, reports, opinions and analysis disclosed to the Customer by Hi-Speed. Hi-Speed shall not be liable for any errors or omissions, or any losses, injury or damages arising from the use of such information, reports, opinions and analysis by the Customer.



38.	Drive End Lubrication Type	(Grease) Grease Lubricated	
39.	Drive End Bearing Insulation or Grounding Device?		
	 None		
40.	Drive End Wavy Washer/Snap-Ring Other Retention Device?	none	
41.	Drive End Bearing Condition	replace/frosting	P79
			
42.	Opposite Drive End Bearing Number	6210	
43.	Opposite Drive End Bearing Quantity	1	
44.	Opposite Drive End Bearing Type	(Ball) Ball Bearing	P100
			
45.	Opposite Drive End Lubrication Type	(Grease) Grease Lubricated	
46.	Opposite Drive End Bearing Insulation or Grounding Device?		
	 None		
47.	Opposite Drive End Wavy Washer/Snap-Ring Other Retention Device?	none	
48.	Opposite Drive End Bearing Condition	replace/frosted	P114

Hi-Speed Industrial Service disclaims all warranties, both express and implied, relating to the information, reports, opinions and analysis disclosed to the Customer by Hi-Speed. Hi-Speed shall not be liable for any errors or omissions, or any losses, injury or damages arising from the use of such information, reports, opinions and analysis by the Customer.



49. Signature of Technician who Performed Teardown

Terrence Holland

50. List Parts Needed Prior to Reassembly

#### Mechanical Fits - Armature

51. Coupling Fit Closest to Bearing Housing

0 Degrees

60 degrees

120 degrees

52. Coupling Fit Closest to the End of the Shaft

0 Degrees

60 degrees

120 degrees

53. Drive End Bearing Shaft Fit

0 Degrees

60 Degrees

120 Degrees

2.1659

2.1657

2.1658

54. Drive End Bearing Shaft Fit Condition

(P) Pass

55. Opposite Drive End Bearing Shaft Fit

0 Degrees

60 Degrees

120 Degrees

1.9688

1.9687

1.9687

56. Opposite Drive End Bearing Shaft Fit Condition

(P) Pass

57. Shaft Air Seal Fits

Drive End Air Seal

Opposite Drive End Air Seal

#### Mechanical Fits- Bearing Housings



58. Drive End - End Bell Bearing Fit

0 Degrees

60 Degrees

120 Degrees

3.939

3.939

59. Drive End - Endbell Bearing Fit Condition

(F) Fail

60. Opposite Drive End - End Bell Bearing Fit

0 Degrees

60 Degrees

120 Degrees

61. Opposite Drive End - Endbell Bearing Fit Condition

(F) Fail

ODE housing fit requires insulated fit

Hi-Speed Industrial Service disclaims all warranties, both express and implied, relating to the information, reports, opinions and analysis disclosed to the Customer by Hi-Speed. Hi-Speed shall not be liable for any errors or omissions, or any losses, injury or damages arising from the use of such information, reports, opinions and analysis by the Customer.

Drive End

Opposite Drive End

pass

pass



63. End Bell Air Seal Fits

Drive End Air Seal

Opposite Drive End Air Seal

64. List any Machine work Needed Below

D.E &amp; ODE housing fits bad

*ODE housing fit requires insulated fit.*

65. Signature of Technician Performing Measurements

Terrence Holland

**Root Cause of Failure**

66. Failure Locations

P8

*D.e and ode bearings, and comm requires polishing.*

*Motor has no shaft current protection i.e. aegis shaft grounding ring or insulated housing fit or bearing. Both bearings show evidence of electrical discharge machining in the form of frosting.*



### Commutator Data

68. Total Copper Segment Length

69. Number of Bars

70. Number of Wires Per Copper Bar and Size

Number of Wires per Bar	Wire Size

71. Equalizers per Copper Bar and Equalizer Wire Size

Equalizers per Bar	Wire Size

72. Document Commutator Diameter, Minimum and Max

Current Comm Diameter	Minimum Comm Diameter	Maximum Comm Diameter

73. Commutator Shaft Diameter

Front Shaft Diameter	Back Shaft Diameter

74. Commutator Type

75. Commutator Bore

76. Signature of Technician Recording Data

### Dynamic Balance Report

77. Rotor Weight and Balance Grade

Rotor Weight	Balance Grade

78. Initial Balance Readings

Drive End Readings	Opposite Drive End Readings

79. Final Balance Readings

Drive End Readings	Opposite Drive End Readings

80. Signature of the Balance Technician

### Post Armature Rewind Testing

81. Post Rewind Armature Insulation Resistance to Ground

82. Post Rewind Field Circuit Measure the Insulation Resistance to Ground



83.	Post Rewind Armature Number of Bars - Bar to Bar Test		
	Number of Bars	Bar to Bar Test	
84.	Post Rewind Field Circuit Insulation Resistance to Ground		
85.	Post Rewind Interpole Circuit Insulation Resistance to Ground		
86.	Post Rewind Field Drop Test Fields 1&2		
	Total AC Voltage	Field #1	Field #2
87.	Post Rewind Field Drop Test Fields 3&4		
	Field #3	Field #4	
88.	Post Rewind Field Drop Test Fields 5&6		
	Field #5	Field #6	
89.	Post Rewind Field Drop Test Fields 7&8		
	Field #7	Field #8	
90.	Post Rewind Interpole Drop Test 1&2		
	Total AC Voltage	Interpole #1	Interpole #2
91.	Post Rewind Interpole Drop Test 3&4		
	Interpole #3	Interpole #4	
92.	Post Rewind Interpole Drop Test 5&6		
	Interpole #5	Interpole #6	
93.	Post Rewind Interpole Drop Test 7&8		
	Interpole #7	Interpole #8	
Post Mechanical Repair			
94.	Post Repair Coupling Fit Closest to Bearing Housing		
	0 Degrees	60 degrees	120 degrees
95.	Post Repair Coupling Fit Closest to the End of the Shaft		
	0 Degrees	60 degrees	120 degrees
96.	Post Repair Drive End Bearing Shaft Fit		
	0 Degrees	60 Degrees	120 Degrees
97.	Post Repair Drive End Bearing Shaft Fit Condition		
98.	Post Repair Drive End Opposite Drive End Bearing Shaft Fit		
	0 Degrees	60 Degrees	120 Degrees
99.	Post Repair Drive End Opposite Drive End Bearing Shaft Fit Condition		
100.	Post Repair Drive End - End Bell Bearing Fit		
	0 Degrees	60 Degrees	120 Degrees

Hi-Speed Industrial Service disclaims all warranties, both express and implied, relating to the information, reports, opinions and analysis disclosed to the Customer by Hi-Speed. Hi-Speed shall not be liable for any errors or omissions, or any losses, injury or damages arising from the use of such information, reports, opinions and analysis by the Customer.

101.	Post Repair Drive End - Endbell Bearing Fit Condition		
102.	Post Repair Opposite Drive End - End Bell Bearing Fit		
	0 Degrees	60 Degrees	120 Degrees
103.	Post Repair Opposite Drive End - Endbell Bearing Fit Condition		
104.	Post Repair Bearing Cap Condition		
	Drive End	Opposite Drive End	
105.	Post Repair End Bell Air Seal Fits		
	Drive End Air Seal	Opposite Drive End Air Seal	
106.	Signature of Tech Performing Mechanical Repairs		
<b>Assembly</b>			
107.	Take Pictures of all Major Components Prior to Reassembly		
108.	Verify Brush Box Holders Have the Proper Clearance, and Brushes have been Seated Properly		
109.	Assembled Shaft End Play and Runout		
	Shaft Endplay	Shaft Runout	
110.	Perform No-Load Test Run, Record Armature Voltage and Current		
	Voltage	Current	
111.	Perform No-Load Test Run, Record Field Voltage and Current		
	Voltage	Current	
112.	Document Vibration Readings Drive End		
	Horizontal	Vertical	Axial
113.	Document Vibration Readings Opposite Drive End		
	Horizontal	Vertical	Axial
114.	Perform Full-Load Test Run, Record Armature Voltage and Current		
	Voltage	Current	
115.	Perform Full-Load Test Run, Record Field Voltage and Current		
	Voltage	Current	
116.	Document Vibration Readings Under Full Load Drive End		
	Horizontal	Vertical	Axial
117.	Document Vibration Readings Under Full Load Opposite Drive End		
	Horizontal	Vertical	Axial
118.	Ambient Temperature		
119.	Drive End Bearing Temps Under Full Load		
	5 Minutes	10 Minutes	15 Minutes

120. Opposite Drive End Bearing Temps Under Full Load			
5 Minutes	10 Minutes	15 Minutes	
121. Final Test Run Sign-Off			
122. Document Final Condition With Pictures			
123. Final QC Sign-Off			
