

Job Information

Job #:	94793				Date:	December 10, 2018
Priority:	_	Authorized OT:	No	Authorized by:		

Customer Information

Name: Wright's Cabinets Motor#:

Name Plate Information

ADDA	Enclosure :	Totally Enclosed Fan Cooled	Horsepower/kW:	13 kW
7061475	Model#:	FC132M/2	Service Factor:	
132M	Rated RPM:	3492	Rated Voltage:	230/460
3	Rated Amps:	44/22	Cycles:	60
	7061475 132M	7061475 Model#: 132M Rated RPM:	Fan Cooled 7061475 Model#: FC132M/2 132M Rated RPM: 3492	Fan Cooled7061475Model#:FC132M/2Service Factor:132MRated RPM:3492Rated Voltage:

Special design: No

VUEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



AC Electrical Inspection

Megs at reasseml	oly: Good	Surge at reassembly:	Good	Hi-pot reassembly: Good			
Winding Resistance Incoming							
	Phases A to B	Phases B to C	Phases C to A	Resistive imbalance			
Outgoing	0.669	0.670	0.668	0.2			
Test Run Inspection Date December 10, 2018							
— I have merged this motor and verified that all electrical tests are complete!							
Power Supply							

	Phase A	Phase B	Phase C
No Load Voltage	462	459	460
No Load Current	7.4	7.2	6.6

Temperatures: (Degrees Fahrenheit)

Test run ball-bearing motors for 15 minutes.

Test run sleeve bearing motors for 60 minutes.

Temperature rise at the end of test run should be less than 2° every five minutes.

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



MILLINGTON, TN LITTLE ROCK, AR


Test Run Inspection (Continued)

Ambient Temp:

TIME	DE	Degree Change	ODE	Degree Change
START:				
5 MIN:				
10 MIN:				
15 MIN:				
20 MIN:				
25 MIN:				
30 MIN:				
35 MIN:				
40 MIN:				
45 MIN:				
50 MIN:				
55 MIN:				
60 MIN:				



Test Run Inspection (Continued)

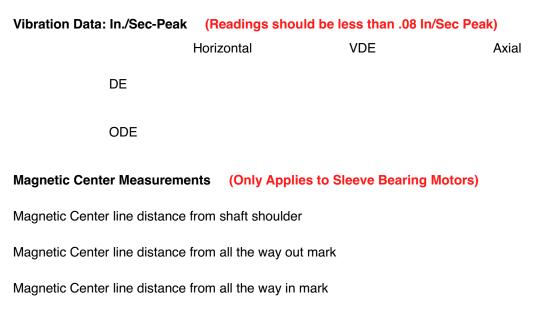

Total Motor End Float

Additional photos







Yes, the shaft has been isolated for delivery.

Service Tech name:

Lynn McDonald

Service Tech signature:

Lynn Madonald

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301
