

Job Information

Job #:	94944				Date:	December 11, 2018
Priority:	_	Authorized OT:	No	Authorized by:		

Customer Information

Name: WELSPUN Motor#:

Name Plate Information

Manufacturer:	Wet	Enclosure :	Totally Enclosed Fan Cooled	Horsepower/kW:	185KW
Serial#:	DERA315-22	Model#:	1ETEIFR1XX1600 40	Service Factor:	1.15
Frame:	315S/M4	Rated RPM:	1780	Rated Voltage:	460
Phase:	3	Rated Amps:	271	Cycles:	60

Special design: No

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



AC Electrical Inspection

Megs at reassem	bly: Go	ood	Surge at reassembly:	Good	Hi-po	t reassembly:	Good
Winding Resista	nce Incon	ning					
	Phases A	to B	Phases B to C	Phases C to A		Resistive imbala	nce
Outgoing	15.898		16.258	16.218		2.0	

Test Run Inspection

Date December 11, 2018

Yes I have merged this motor and verified that all electrical tests are complete!

Power Supply

	Phase A	Phase B	Phase C
No Load Voltage	460	457	458
No Load Current	87.4	85.6	85.1

Temperatures: (Degrees Fahrenheit)

Test run ball-bearing motors for 15 minutes.

Test run sleeve bearing motors for 60 minutes.

Temperature rise at the end of test run should be less than 2° every five minutes.

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



MILLINGTON, TN LITTLE ROCK, AR


Test Run Inspection (Continued)

Ambient Temp:

TIME	DE	Degree Change	ODE	Degree Change
START:				
5 MIN:				
10 MIN:				
15 MIN:				
20 MIN:				
25 MIN:				
30 MIN:				
35 MIN:				
40 MIN:				
45 MIN:				
50 MIN:				
55 MIN:				
60 MIN:				



Test Run Inspection (Continued)

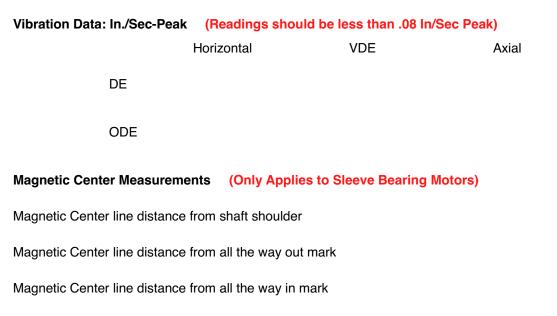

Total Motor End Float

Additional photos









Yes, the shaft has been isolated for delivery.

Service Tech name:

Robert Wiley

Service Tech signature:



WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301
