

Job Information

| Job #: | 95175 | | | | Date: | March 20, 2019 |
|-----------|-------|----------------|----|----------------|-------|----------------|
| Priority: | _ | Authorized OT: | No | Authorized by: | | |

Customer Information

Name: Remington Motor#:

Name Plate Information

| Manufacturer: | DC MORRISON CO | Enclosure : | Open Drop Proof (ODP) | Horsepower/kW: | 1 |
|---------------|----------------|-------------|--------------------------|-----------------|-----|
| Serial#: | 41259M-LHM | Model#: | LA2B | Service Factor: | |
| Frame: | 184 | Rated RPM: | 1725/3450 | Rated Voltage: | 480 |
| Phase: | 3 | Rated Amps: | 2.05/1.75 | Cycles: | 60 |
| | | | | | |

Special design: No

VEST TENNESSE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



AC Electrical Inspection

| Megs at reassemb | oly: Good | Surge at reassembly: | Good | Hi-pot reassembly: Good | | |
|---|---------------|----------------------|---------------|-------------------------|--|--|
| Winding Resistance Incoming | | | | | | |
| | Phases A to B | Phases B to C | Phases C to A | Resistive imbalance | | |
| Outgoing | 9.161 | 9.158 | 9.147 | 0.1 | | |
| Test Run Inspection Date March 20, 2019 | | | | | | |
| — I have merged this motor and verified that all electrical tests are complete! | | | | | | |
| Power Supply | | | | | | |

| | Phase A | Phase B | Phase C |
|-----------------|---------|---------|---------|
| No Load Voltage | 458 | 455 | 454 |
| No Load Current | 1.6 | 1.5 | 1.6 |

Temperatures: (Degrees Fahrenheit)

Test run ball-bearing motors for 15 minutes.

Test run sleeve bearing motors for 60 minutes.

Temperature rise at the end of test run should be less than 2° every five minutes.

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



MILLINGTON, TN LITTLE ROCK, AR


Test Run Inspection (Continued)

Ambient Temp:

| TIME | DE | Degree Change | ODE | Degree Change |
|---------|----|---------------|-----|---------------|
| START: | | | | |
| 5 MIN: | | | | |
| 10 MIN: | | | | |
| 15 MIN: | | | | |
| 20 MIN: | | | | |
| 25 MIN: | | | | |
| 30 MIN: | | | | |
| 35 MIN: | | | | |
| 40 MIN: | | | | |
| 45 MIN: | | | | |
| 50 MIN: | | | | |
| 55 MIN: | | | | |
| 60 MIN: | | | | |



Test Run Inspection (Continued)

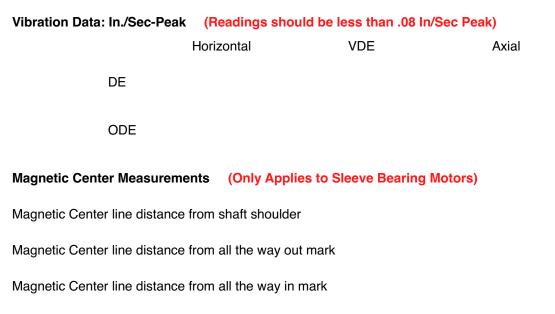

Total Motor End Float

Additional photos








Yes, the shaft has been isolated for delivery.

Service Tech name:

Robert Wiley

Service Tech signature:



WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301
