

Job Information

Job #:	95292				Date:	April 1, 2019
Priority:	_	Authorized OT:	No	Authorized by:		

Customer Information

Name: Delta Plastic Motor#:

Name Plate Information

Manufacturer:	Baldor	Enclosure :	Open Drop Proof (ODP)	Horsepower/kW:	150
Serial#:	M9129530-010001L Q	Model#:		Service Factor:	
Frame:	URL7882	Rated RPM:	1755/2000	Rated Voltage:	460
Phase:	3	Rated Amps:	180	Cycles:	60

Special design: No

VEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



AC Electrical Inspection

Megs at reassemb	oly: Good	Surge at reassemb	bly: Good	Hi-pot reassembly: Good		
Winding Resistance Incoming						
	Phases A to B	Phases B to C	Phases C to <i>i</i>	A Resistive imbalance		
Outgoing	51.988	51.979	51.882	0.4		
Test Run Inspection Date April 1, 2019						
— I have merged this motor and verified that all electrical tests are complete!						
Power Supply						
	-	Phase A	Phase B	Phase C		
No Load Voltage		459	455	455		

No Load Current 51.9 52.7 49.6

Temperatures: (Degrees Fahrenheit)

Test run ball-bearing motors for 15 minutes.

Test run sleeve bearing motors for 60 minutes.

Temperature rise at the end of test run should be less than 2° every five minutes.

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



MILLINGTON, TN LITTLE ROCK, AR


Test Run Inspection (Continued)

Ambient Temp:

TIME	DE	Degree Change	ODE	Degree Change
START:				
5 MIN:				
10 MIN:				
15 MIN:				
20 MIN:				
25 MIN:				
30 MIN:				
35 MIN:				
40 MIN:				
45 MIN:				
50 MIN:				
55 MIN:				
60 MIN:				



Test Run Inspection (Continued)

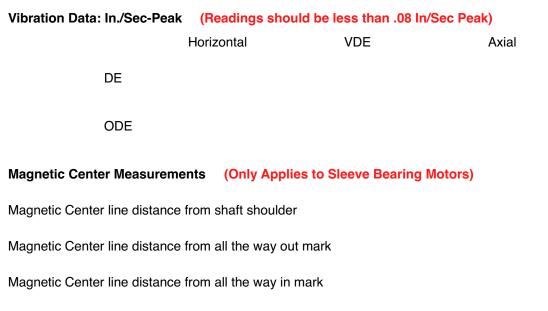

Total Motor End Float

Additional photos









Yes, the shaft has been isolated for delivery.

Service Tech name:

Robert Wiley

Service Tech signature:



WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301
