

### **Job Information**

Job #:	95580				Date:	June 25, 2019
Priority:	_	Authorized OT:	No	Authorized by:		

# **Customer Information**

Name:	Almatis	Motor#:

### **Name Plate Information**

Manufacturer:	Reliance	Enclosure :	Totally Enclosed Non-Ventilated	Horsepower/kW:	1.5
Serial#:		Model#:		Service Factor:	
Frame:	182TDZ	Rated RPM:	1755	Rated Voltage:	230/460
Phase:	3	Rated Amps:	5/2.5	Cycles:	60

Special design: No

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301



# **AC Electrical Inspection**

Megs at reassem	bly: Good	Surge at reassembly:	Good	Hi-pot reassembly:	Good		
Winding Resistance Incoming							
	Phases A to B	Phases B to C	Phases C to A	Resistive imbalar	ICE		
Outgoing	0.00	0.00	0.00	0.00			
Test Run I	nspection		Date	June 25, 2019			
Yes	I have merged this motor and verified that all electrical tests are complete!						

	Phase A	Phase B	Phase C
No Load Voltage	457	456	457
No Load Current	1.6	1.7	1.6

### **Temperatures: (Degrees Fahrenheit)**

#### Test run ball-bearing motors for 15 minutes.

#### Test run sleeve bearing motors for 60 minutes.

Temperature rise at the end of test run should be less than 2° every five minutes.

WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301

**Power Supply** 



## MILLINGTON, TN LITTLE ROCK, AR


# **Test Run Inspection (Continued)**

#### Ambient Temp:

TIME	DE	Degree Change	ODE	Degree Change
START:				
5 MIN:				
10 MIN:				
15 MIN:				
20 MIN:				
25 MIN:				
30 MIN:				
35 MIN:				
40 MIN:				
45 MIN:				
50 MIN:				
55 MIN:				
60 MIN:				



### **Test Run Inspection (Continued)**

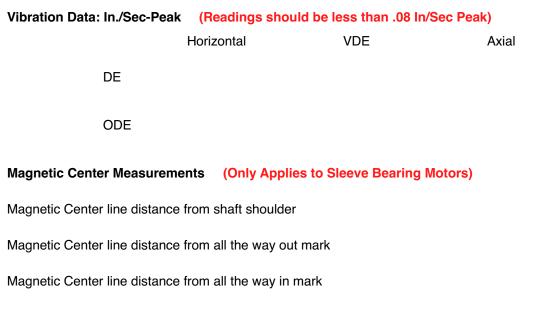

Total Motor End Float

### **Additional photos**









Yes, the shaft has been isolated for delivery.

Service Tech name:

Robert Wiley

Service Tech signature:



WEST TENNESSEE 7030 Ryburn Drive Millington, TN 38053 Phone 901-873-5300 Fax 901-873-5301
